

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



REPAIRING OF TILES



INSTALLATION OF FEEDER PILLAR

**TOWER-1 (TYPE A-1) (Overall completion 91.85 %)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – Fixing of false ceiling in toilets, Glass fixing in Aluminum windows & ventilators, Internal Painting, Repairing of Ext plaster and Fixing of Fire Doors etc.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



FIXING OF TILES IN BED ROOMS



FIXING OF GREEN MARBLE IN CORRIDOR



BRICK COBA AT TERRACE FLOOR

### **TOWER 2 (TYPE A-1) (Overall completion 78.40 %)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – Fixing of Vitrified tiles in bed rooms, Green marble in corridor at 10<sup>th</sup>, floor, Kota stone flooring in corridor, water proofing in toilets wall tiles in Kitchen & toilets, brick coba at terrace floor. External primer in progress.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



FIXING OF WALL TILES IN



EXTERNAL PLASTER IN BALCONY

**TOWER-3 (TYPE A-1) (Overall completion 67.20 %)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – External & Internal plaster, Fixing of door frame & Fixing of wall tiles in toilets & kitchen, Green marble in corridor, Plumbing works, RCC works in terrace, Water proofing toilets & kitchen ,Kota stone in corridor and podium etc.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



EXTERNAL PLASTER



FIXING OF DOOR FRAMES

**TOWER-4 (TYPE A-1) (Overall completion Approx 65%)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – External & Internal plastering, RCC works in terrace, Fixing of Doors frame, Fixing of Aluminum frame, Water proofing in toilet & Kitchen, Plumbing works, Fixing of grills in corridor etc.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



FIXING OF KOTA STONE AT PODIUM



POP WORK



EXTERNAL PLASTER

**TOWER-5 (TYPE A-2) (Overall completion 73.00 %)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – External plaster of flat 1, Fixing of Green marble in corridor at 4<sup>rd</sup> floor, Fixing of Kota stone at podium, Shuttering of wall of OH water tank, POP cornice in bed rooms etc**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



GRINDING OF KOTA STONE AT PODIUM



PAINTING IN CORRIDOR

**TOWER-6 (TYPE A-2) (Overall completion 86.10 %)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – Internal painting in flats at 7th floor, fixing of false ceiling in toilets, Grinding of Kota stone of podium Fixing of glass in aluminum windows etc.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



PREPARATION FOR PCC



BRICK WORK OF GARBAGE ROOM



FIXING OF SERVICE COUNTER IN KITCHEN



FIXING OF TILES AT 11<sup>TH</sup> FLOOR

**TOWER-7 (TYPE B-1) (Overall completion 87.70 %)**

**Total Floor – Stilt + 11**

**Total flat = 119**

**Progress – Floor and wall tiles fixing, Granite fixing in Kitchen plat form, Aluminum frame fixing in windows, Brick work of Garbage room at stilt floor, Preparation of stilt for PCC.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



OBD IN LIVING ROOM



WHITE WASH AT STILT FLOOR

**TOWER- 8 (TYPE B-1 & TYPE B2) (Overall completion 87.30 %)**

**Total Floor – Stilt + 11**

**Total flat = 33.**

**Progress – Fixing of main frame of aluminium in widows & Internal Paiting ,  
White wash at stilt floor etc.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017



**FIXING OF KOTA STONE AT  
STAIRCASE**



**WATER PROOFING OF  
SWIMMING POOL**

**COMMUNITY CENTRE - (Overall completion 92.00 %)**

**Total floor – Basement +03**

**Progress – Fixing of Kota stone at staircase towards of swimming pool.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017




**FACILITY BLOCK - (Overall completion 95.15 %)**

**Total floor – Ground +01**

**Progress – Internal OBD 1st coat & painting on Staircase railing.**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017

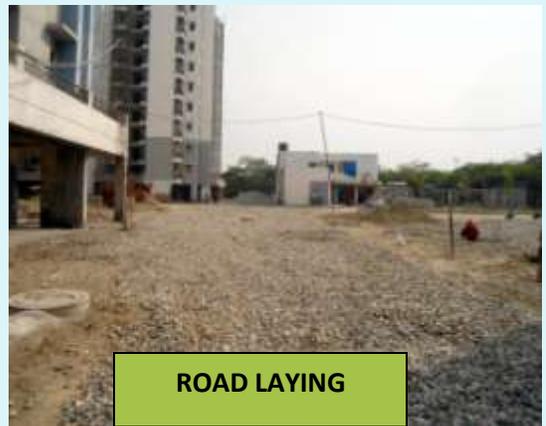

Gate No. 1 - (Overall completion 90.00 %)

Progress – Road work in progress 11.00% & Fixing of Kota stone in Visitor's Room.


## **PROGRESS MEERUT PROJECT AS ON 15 MAY 2017**



**STP - (Overall completion 37.26 %)**

**Civil work completed in 2013, No progress in electro mechanical works,  
excepted to commence by Sep 2017**

## PROGRESS MEERUT PROJECT AS ON 15 MAY 2017

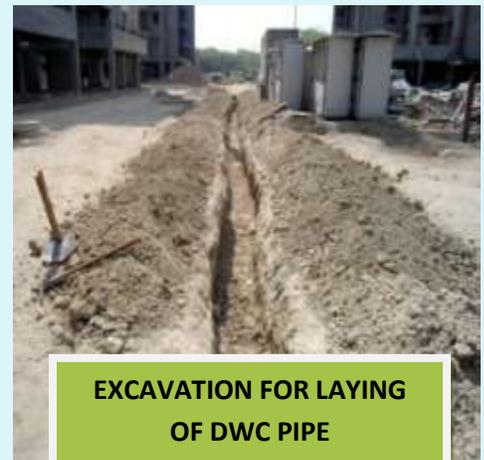

EXCAVATION FOR LAYING  
OF DWC PIPE



FEADER PILLAR

**SUB Station - (Overall completion 96.00 %)**

**Progress – Generators, Transformers installed in 2013, HT/LT cables and control panels procured, Servicing of DG stes and Tranformers initiated, Fixinf of feadar pillar near Tower 1& 6 .**
