

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



GAIL GAS PIPE LINE IN PROGRESS



ALUMINUM WINDOWS FIXING

### **TOWER-1 (TYPE A-1)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – Inside Painting, GAIL GAS pipe line, Repairing of Ext Plaster, Glass fixing in Aluminum windows, Fixing of Fir Doors and False ceiling in Toilet etc.**

**Overall completion 92.10 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



FIXING OF HDF DOOR SHUTTERS



GRANITE ON WASH BASIN COUNTER



FIXING OF TILES IN BALCONY

### TOWER 2 (TYPE A-1)

Total Floor – Stilt + 10

Total flat = 60

Progress – Fixing of Granite, Tiles Flooring, Kota stone Flooring in corridor, Water proofing in toilet, Finishing of OH Water tank, Internal & Ext plumbing works etc.

Overall completion 77.50 %

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



EXTERNAL PLASTER



CEILING PLASTER IN CORRIDOR

### **TOWER-3 (TYPE A-1)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – External & Internal plaster, Fixing of door frame & Green marble in corridor, plumbing works, RCC work in terrace, Water proofing in toilets, Kota stone fixing in podium and steps, Fixing of Grills in common area etc**

**Overall completion 65.50 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



### **TOWER-4 (TYPE A-1)**

**Total Floor – Stilt + 10**

**Total flat = 60**


**Progress – External & Internal plaster, RCC Work in terrace, Fixing of Door frames, Fixing of Aluminum soft frame, Water proofing in toilets, Plumbing works, Kota stone fixing over podium, Fixing of Grills in common area etc**

**Overall completion 64.00 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



WATER PROOFING IN PODIUM SLAB

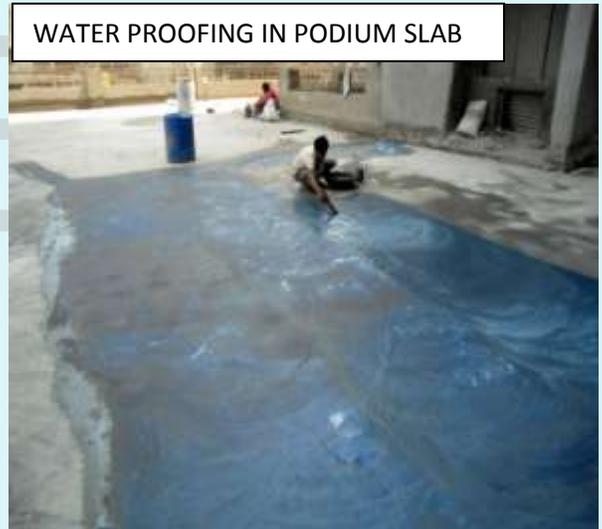

### **TOWER-5 (TYPE A-2)**

**Total Floor – Stilt + 10**

**Total flat = 60**

**Progress – External plaster, Fixing of Vitrified tiles, Water proofing over podium slab, RCC Terrace works, Fixing of Grills in common area, POP inside flats etc**

**Overall completion 71.00 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



FIXING OF FIRE DOOR



FALSE CEILING WORK IN TOILET



INTERNAL PAINTING

### **TOWER-6 (TYPE A-2)**

**Total Floor – Stilt + 10**

**Total flat = 60**


**Progress – Internal Painting in flats, Fixing of floor tiles & False ceiling in toilets, Fixing of Fire Doors etc.**

**Overall completion 85.50%**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



BRICK WORK BELOW KITCHEN COUNTER

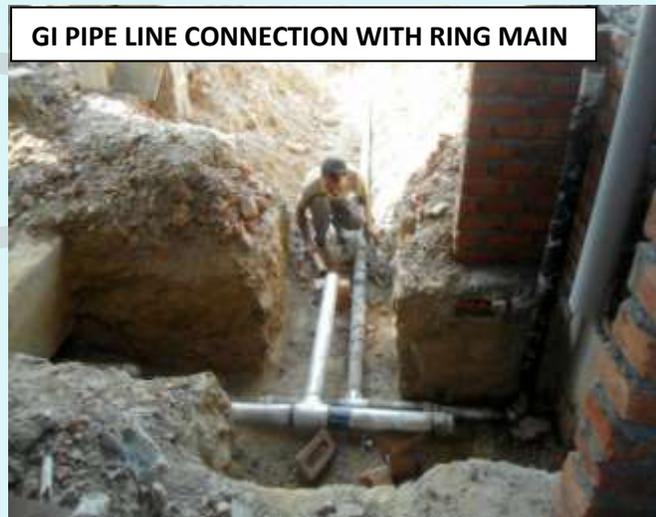

GI PIPE LINE CONNECTION WITH RING MAIN

### **TOWER-7 (TYPE B-1)**

**Total Floor – Stilt + 11**

**Total flat = 119**

**Progress Wall tiles fixing in toilets, Granite fixing on wash basin counters, Aluminum frame fixing in windows, Brick work of partition wall in kitchen, GI pipe line connection with ring main for water supply to OH water tank.**

**Overall completion 85.00 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



### **TOWER- 8 (TYPE B-1 & TYPE B2)**

**Total Floor – Stilt + 11**

**Total flat = 33.**

**Progress – Fixing of main frame of aluminium in widows & Gail Gas pipe line work.**

**Overall completion 87.00 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



FIXING OF GREEN MARBLE ON PLANTER




**Total floor – Basement +03**

**Progress – Fixing of Green marble on panter.**

**COMMUNITY CENTRE - Overall completion 92.00 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017

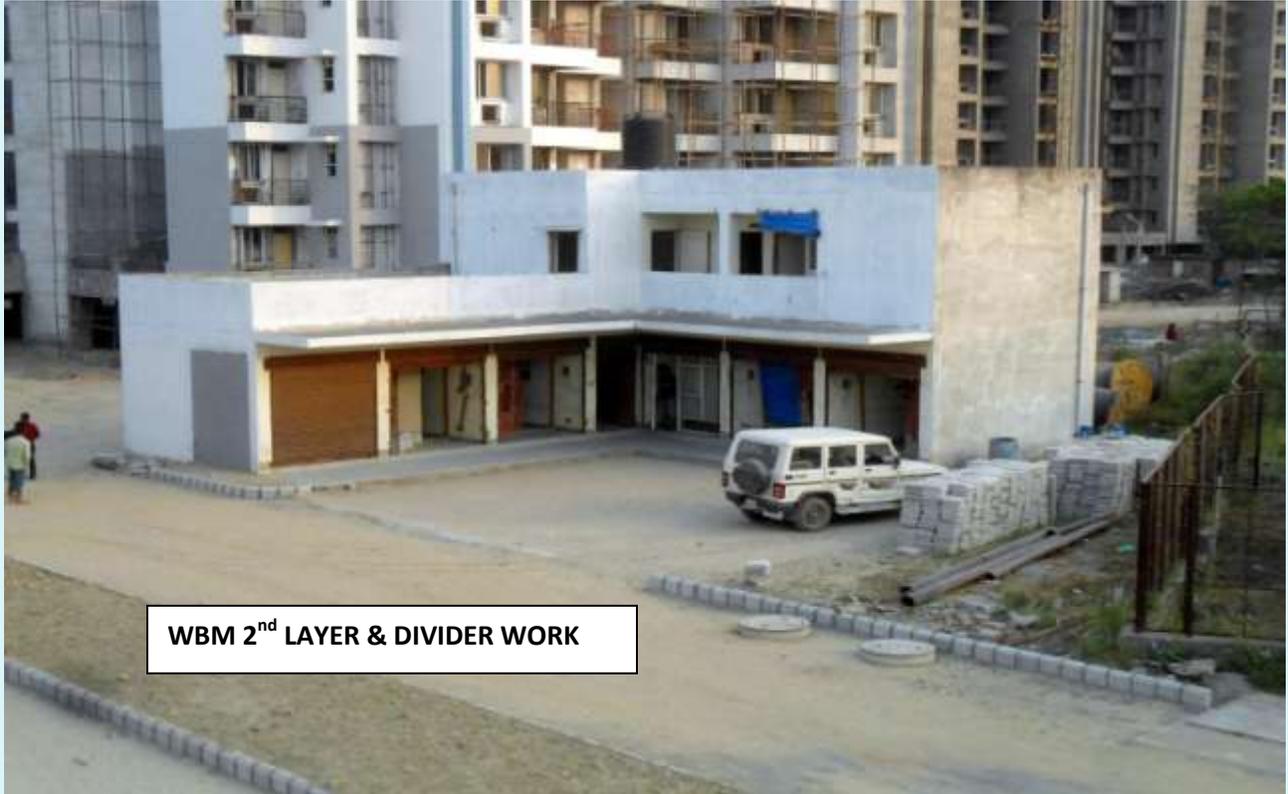

**Total floor – Ground +01**

**Progress – No progress.**

**FACILITY BLOCK - Overall completion 95.15 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



ROAD WORK IN PROGRESS NEAR BLOCK 6



### **GATE NO. 1**

**Progress – Road work in progress**

**Overall completion 90.00 %**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



**STP - (Overall completion 37.26 %)**

**Progress – No progress.**

## PROGRESS MEERUT PROJECT AS ON 15 APR 2017



**Power house - Overall completion 96.00 %**

**Progress – Generators, transformers, HT/LT cables and control panels procured and placed 2 Years back. Awaiting Energising after necessary servicing by the company .**
