

## **TOWER-1A: TERRACE FLOOR SLAB**



**TOWER NO: 1A (Overall completion 74.00%)**

**Total Floors: - Stilt + 12 Upper floors**

**Total Flats: - 24 (Duplex Type-A1)**

### **PROGRESS:**

1. **Structural works up to terrace floor slab completed.**
2. **12<sup>th</sup> floor concrete block masonry work completed & terrace floor parapet wall block masonry work completed.**
3. **Staircase headroom column concrete work completed and head room slab concrete work completed. Head room block work, lift machine room and OHT work in progress.**
4. **Internal wall and ceiling plastering work completed up to 12<sup>th</sup> floor.**
5. **5<sup>th</sup> and 6<sup>th</sup> floor door frame fixing work in progress.**
6. **Internal waterproofing work completed up to 12<sup>th</sup> floor.**
7. **Tiling work completed up to 6<sup>th</sup> floor, 7<sup>th</sup> and 8<sup>th</sup> floor in progress.**
8. **3<sup>rd</sup> and 4<sup>th</sup> floor toilet flooring and wall dadoing work in progress.**
9. **Balcony railing work completed up to 10<sup>th</sup> floor. 11<sup>th</sup> floor in progress.**
10. **Internal staircase railing work completed up to 12<sup>th</sup> floor.**
11. **Internal wall electrical conduiting work completed up to 12<sup>th</sup> floor. 1<sup>st</sup> floor internal electrical wiring work completed, 2<sup>nd</sup> floor wiring work in progress.**
12. **Internal plumbing work (CPVC) and (SWR PVC) pipe work completed up to 12<sup>th</sup> floor.**
13. **External plastering work (South, East, West, North side) in progress.**
14. **Door shutters fixing work completed up to 3<sup>rd</sup> floor.**
15. **1<sup>st</sup> to 6<sup>th</sup> floor internal wall putty work (first coat) in progress.**
16. **External staircase railing work in progress.**

## **TOWER-1B: TERRACE FLOOR SLAB**



**TOWER NO: 1B (Overall completion 74.20%)**

**Total Floors:** - 2 Stilts + 12 Upper floors

**Total Flats:** - 24 (Duplex Type-A1)

### **PROGRESS:**

1. Structural works up to terrace floor slab completed. Lift machine room and OHT work in progress.
2. Terrace floor parapet wall block masonry work completed.
3. Concrete block masonry work completed up to 12th floor.
4. Internal wall and ceiling plastering work completed up to 12<sup>th</sup> floor.
5. Tiling work completed up to 8<sup>th</sup> floor.
6. Door frame fixing work completed up to 10<sup>th</sup> floor.
7. Balcony railing work completed up to 10<sup>th</sup> floor.
8. Internal staircase railing work completed up to 10<sup>th</sup> floor. 11<sup>th</sup> floor in progress.
9. 1<sup>st</sup> and 2<sup>nd</sup> floor internal staircase cuddapah stone work in progress.
10. Internal waterproofing work completed up to 12<sup>th</sup> floor.
11. Internal wall electrical conduiting work completed up to 12<sup>th</sup> floor.
12. Internal plumbing (CPVC) work completed up to 12<sup>th</sup> floor, and internal (SWR PVC) pipe work completed up to 12<sup>th</sup> floor.
13. External plastering work (South, East, West, North side) in progress.
14. 3<sup>rd</sup> floor toilet wall dadoing work in progress.
15. 1<sup>st</sup> to 8<sup>th</sup> floor door shutter fixing work in progress.
16. 1<sup>st</sup> to 4<sup>th</sup> floor internal wall putty work (first coat) in progress.

## **TOWER-1C: TERRACE FLOOR SLAB**



**TOWER NO: 1C (Overall completion 67.30%)**

**Total Floors:** - Stilt + 12 Upper floors

**Total Flats:** - 24 (Duplex Type-A1)

### **PROGRESS:**

1. Structural work up to terrace floor slab completed. Head room column reinforcement and concrete work in progress.
2. Concrete block masonry work completed up to 11<sup>th</sup> floor.
3. 10<sup>th</sup> floor internal wall plastering work in progress.
4. Tiling work completed up to 4<sup>th</sup> floor, 5<sup>th</sup> floor in progress. 4<sup>th</sup> floor toilet dadoing work in progress.
5. 1<sup>st</sup> and 2<sup>nd</sup> floor internal staircase cuddapah stone work in progress.
6. Internal waterproofing work completed up to 10<sup>th</sup> floor.
7. 3<sup>rd</sup> & 4<sup>th</sup> floor door frame fixing work in progress.
8. Balcony railing work completed up to 10<sup>th</sup> floor.
9. Internal Staircase railing work completed up to 6<sup>th</sup> floor, 7<sup>th</sup> floor in progress.
10. Internal wall electrical conduiting work completed up to 10<sup>th</sup> floor.
11. Internal plumbing (CPVC) work completed up to 10<sup>th</sup> floor, internal (SWR PVC) pipe work completed up to 9<sup>th</sup> floor.
12. External plastering work (South, East, North and West side) in progress.
13. 1<sup>st</sup> and 2<sup>nd</sup> floor internal wall putty work (first coat) in progress.

## **TOWER-2B: TERRACE FLOOR SLAB**



**TOWER NO: 2B (Overall completion 63.80%)**

**Total Floors:** - 2 Stilts + 12 Upper floors

**Total Flats:** - 48 (Simplex Type-A2)

### **PROGRESS:**

1. Structural works completed up to terrace floor.
2. Staircase headroom slab completed. Lift machine room and OHT work in progress.
3. Concrete block masonry work completed up to 12<sup>th</sup> floor and terrace floor parapet wall block masonry work completed.
4. 12<sup>th</sup> floor internal plastering work in progress.
5. Tiling work completed up to 6<sup>th</sup> floor, 3<sup>rd</sup> and 4<sup>th</sup> floor toilet wall dadoing work in progress.
6. Balcony railing work completed up to 10<sup>th</sup> floor.
7. Door frame fixing work completed up to 7<sup>th</sup> floor, 8th floor in progress.
8. Internal wall electrical conduiting work completed up to 11<sup>th</sup> floor. 12<sup>th</sup> floor in progress.
9. Internal plumbing (CPVC) work completed up to 12<sup>th</sup> floor, internal (SWRPVC) pipe work completed up to 9<sup>th</sup> floor.
10. Internal wall putty work 2<sup>nd</sup> to 5<sup>th</sup> floor (first coat) in progress.
11. 1<sup>st</sup> floor to 7<sup>th</sup> floor door shutters fixing work in progress.
12. 11<sup>th</sup> and 12<sup>th</sup> floor internal waterproofing work in progress.
13. External plastering work (North, South, West, and East side) in progress.

## **PROGRESS MYSORE AS ON 15 APRIL 19**

# **TOWER-2C: TERRACE FLOOR SLAB**



**TOWER NO: 2C (Overall completion 61.50%)**

**Total Floors:** - Stilt + 12 Upper floor

**Total Flats:** - 48 (Simplex Type-A2)

### **PROGRESS:**

1. Structural work completed up to terrace floor.
2. Staircase head room slab completed. Lift machine room and OHT work in progress.
3. 11<sup>th</sup> and 12<sup>th</sup> floor concrete block masonry work in progress.
4. 6<sup>th</sup> floor tiling work in progress, 3<sup>rd</sup> floor toilet wall dadoing work in progress.
5. Internal waterproofing work completed up to 10<sup>th</sup> floor.
6. Balcony railing work completed up to 10<sup>th</sup> floor.
7. 7<sup>th</sup> floor door frame fixing work in progress.
8. 10<sup>th</sup> floor internal wall electrical conduiting work in progress.
9. Internal plumbing (CPVC) work completed up to 10<sup>th</sup> floor, internal (SWR PVC) pipe work completed up to 10<sup>th</sup> floor.
10. 1<sup>st</sup> to 5<sup>th</sup> floor door shutters fixing work in progress.
11. 10<sup>th</sup> to 12<sup>th</sup> floor internal wall and ceiling plastering work in progress.
12. External plastering work (North, South, West and East side) in progress.
13. First coat internal wall putty work only 2<sup>nd</sup> floor in progress.

## **PROGRESS MYSORE AS ON 15 APRIL 19**

### **BLOCK-3: SUB STRUCTURE**



**BLOCK NO: 3 (Overall completion 15.30%)**

**Total Floors: - Stilt + 3 Upper floor**

**Amenities: - Club House & Swimming Pool**

#### **PROGRESS:**

- 1. Function hall entrance columns concrete work completed.**
- 2. UG sump tank retaining wall waterproofing work in progress.**
- 3. Back filling work in progress.**
- 4. Swimming pool area retaining wall shuttering work and concrete work in progress.**
- 5. Plinth beam reinforcement and shuttering work and concrete work completed.**
- 6. Pump room slab concrete work completed.**

## **BLOCK-5: TERRACE FLOOR SLAB**



**BLOCK NO: 5 (Overall completion 74.20%)**

**Total Floors:** - Stilt + 10 Upper floors


**Total Flats:** - 40 (Simplex Type B-II)

### **PROGRESS:**

1. **Structural works up to terrace floor slab completed.**
2. **Staircase head room shuttering and bar bending work and lift machine room concrete work in progress.**
3. **Concrete block masonry work completed up to 10th floor & terrace floor parapet wall block masonry work completed.**
4. **Internal wall and ceiling plastering work completed up to 10<sup>th</sup> floor.**
5. **7<sup>th</sup> floor tiling work in progress, 5<sup>th</sup> floor toilet wall dadoing work in progress.**
6. **Balcony railing work completed up to 10<sup>th</sup> floor.**
7. **Water proofing work completed up to 10<sup>th</sup> floor.**
8. **Door frame fixing work completed up to 10<sup>th</sup> floor.**
9. **Internal wall electrical conduiting work completed up to 10<sup>th</sup> floor. 1<sup>st</sup> floor internal electrical wiring work in progress.**
10. **Internal plumbing (CPVC) work completed up to 10<sup>th</sup> floor, internal (SWR PVC) pipe Work Completed up to 10<sup>th</sup> floor.**
11. **External plastering work (North, West, East, and Southside) in progress.**
12. **1<sup>st</sup> to 5<sup>th</sup> floor door shutters fixing work in progress.**
13. **1<sup>st</sup> to 5<sup>th</sup> floor internal wall putty work (first coat) in progress.**

## PROGRESS MYSORE AS ON 15 APRIL 19

# RETAINING WALL

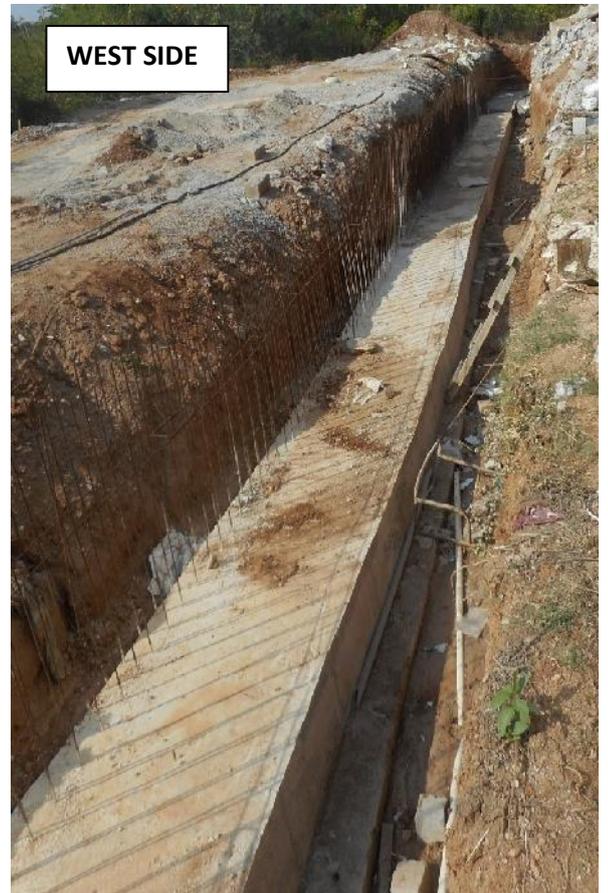

### RETAINING WALL- NORTH AND WEST SIDE

#### PROGRESS:

1. Earth work excavation in progress. North side-90% and west side-97% completed.
2. PCC concrete work in progress. North side-85% and west side-97% completed.
3. Footing and wall reinforcement work in progress. North side-65% and west side-97% completed.
4. Footing concreting work in progress. North side-60% and west side-97% completed.
5. Retaining wall concreting work (first lift) in progress. North side-40% completed and west side not yet commenced.

## COMPOUND WALL



**COMPOUND WALL- SOUTH SIDE**

### **PROGRESS:**

1. Earth work excavation completed.
2. PCC concrete work completed.
3. Plinth beam work completed.
4. Block work in progress. 93% work completed.
5. Outside plastering work in progress. 38% work completed.

**PROGRESS MYSORE AS ON 15 APRIL 19**

## **MAIN ENTRANCE GATE**



**MAIN ENTRANCE GATE- SOUTHSIDE (NEAR BLOCK-3)**

### **PROGRESS:**

- 1. Earth work excavation completed.**
- 2. PCC concrete work completed.**
- 3. Footing and Plinth beam work completed.**
- 4. Column reinforcement work and column starter concreting work completed.**
- 5. Column shuttering work and concreting work not yet commenced.**
