

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

AVERAGE DAILY LABOUR IN MAY- JUN: 348



TOWER NO: A1 OFFICERS (Overall completion-92.07%)

Total floors: S1+S2+8

Total Flats: 32

PROGRESS:

STRUCTURAL WORK	- 100% completed (terrace structure completed)
BRICK WORK	- 100% completed (Except lower & upper stilt)
EXTERNAL PLASTERING	- 95% completed
INTERNAL PLASTERING	- 100% completed
TILING	- 100% completed
PLUMBING	- 100% completed
CHINA WARE FITTING	- 95% completed
PAINTING	- 75% (1st coat paint completed)
EXTERNAL PAINT	-80% completed
ELECTRICAL WORK	- 70% completed
DOOR & WINDOW FIXING	- 90% completed
FIRE FIGHTING WORK	- 35% completed
CP FITTING	-85% completed
BALCONY RAILING	- 70% completed

PROGRESS BHUBANESWAR AS ON 15 JUN 2017



TOWER NO: A2 OFFICERS (Overall completion-80.46%)

Total floors: S1+S2+8

Total Flats: 32

PROGRESS:

STRUCTURAL WORK	- 100% completed (Except terrace structure)
BRICK WORK	- 100% completed (Except lower & upper stilt)
EXTERNAL PLASTERING	- 90% completed
INTERNAL PLASTERING	- 100% completed
TILING	- 65% completed
PLUMBING	- 70% completed
PAINTING	- (only 1 st coat putty completed)
EXTERNAL PAINT	- 25% complete
ELECTRICAL WORK	- 45% completed
FIRE FIGHTING WORK	- 15% completed

PROGRESS BHUBANESWAR AS ON 15 JUN 2017



TOWER NO: A3 OFFICERS (Overall completion-83.99%)

Total floors: S1+S2+8

Total Flats: 32

<u>PROGRESS:</u>	STRUCTURAL WORK	- 100% completed (terrace structure completed)
	BRICK WORK	- 100% completed (Except lower & upper stilt)
	EXTERNAL PLASTERING	- 95% completed
	INTERNAL PLASTERING	- 100% completed
	TILING	- 85% completed
	PLUMBING	- 65% completed
	CHINA WARE FITTING	- 90% completed
	PAINTING	- (only 2 nd coat putty completed)
	EXTERNAL PAINT	-20% completed
	ELECTRICAL WORK	- 55% completed
	DOOR & WINDOW FIXING	- 30% completed
	FIRE FIGHTING WORK	- 15% completed

PROGRESS BHUBANESWAR AS ON 15 JUN 2017



TOWER NO: A4 OFFICERS (Overall completion-84.04%)

Total floors: S1+S2+8

Total Flats: 32

PROGRESS:

STRUCTURAL WORK	- 100% completed (Terrace structure completed)
BRICK WORK	- 100% completed (Except lower & upper stilt)
EXTERNAL PLASTERING	- 95% completed
INTERNAL PLASTERING	- 100% completed
TILING/GRANITE	- 100% completed
PLUMBING	- 100% completed
CHINA WARE FITTING	- 90% completed
PAINTING	- 60% (1 st coat paint completed)
EXTERNAL PAINT	-80% completed
ELECTRICAL WORK	- 65% completed
DOOR & WINDOW FIXING	- 40% completed
FIRE FIGHTING WORK	- 30% completed
CP FITTING	-20% completed

PROGRESS BHUBANESWAR AS ON 15 JUN 2017



TOWER NO: B1 SAILOR (Overall completion-65.06%)

Total floors: S1+S2+11

Total Flats: 43

PROGRESS:

STRUCTURAL WORK	- 100% completed (Except terrace structure)
BRICK WORK	- 95% completed
EXTERNAL PLASTERING	- 90% completed
INTERNAL PLASTERING	- 95% completed
TILING	-05% completed
PLUMBING	- 65% completed
PAINTING	- (only 1 st coat putty up to 10 th floor completed)
ELECTRICAL WORK	- 40% completed
FIRE FIGHTING WORK	- 15% completed

PROGRESS BHUBANESWAR AS ON 15 JUN 2017



TOWER NO: B2 SAILOR (Overall completion-59.46%)

Total floors: S1+S2+11

Total Flats: 43

PROGRESS:

STRUCTURAL WORK	- 100% completed (Except terrace structure)
BRICK WORK	- 95% completed
EXTERNAL PLASTERING	- 10% completed
INTERNAL PLASTERING	- 95% completed
TILING	- To be done
PLUMBING	- 40% completed
PAINTING	- (only 1 st coat putty 11 th floor completed)
ELECTRICAL WORK	- 40% completed
FIRE FIGHTING WORK	- 15% completed

PROGRESS BHUBANESWAR AS ON 15 JUN 2017



TOWER NO: B3 SAILOR (Overall completion-90.42%)

Total floors: S1+S2+11

Total Flats: 42

PROGRESS:

STRUCTURAL WORK	- 100% completed (Terrace structure completed)
BRICK WORK	- 100% completed
EXTERNAL PLASTERING	- 100% completed
INTERNAL PLASTERING	- 100% completed
TILING	- 95% completed
PLUMBING	- 100% completed
PAINTING	- 40% (1st coat paint completed)
EXTERNAL PAINT	-40% completed
CHINA WIRE FITTING	- 80% completed
ELECTRICAL WORK	- 75% completed
DOOR & WINDOW FIXING	- 90% completed
FIRE FIGHTING WORK	- 20% completed
CP FITTING	-85% completed
BALCONY RAILING	- 90% completed
FALSE CEILING	-80% Completed

PROGRESS BHUBANESWAR AS ON 15 JUN 2017



TOWER NO: COMMUNITY CENTER (Overall completion-87%)

Total floors: G+1

PROGRESS:

STRUCTURAL WORK	- 100% completed (Except terrace structure)
BRICK WORK	- 90% completed
EXTERNAL PLASTERING	- 90% completed
INTERNAL PLASTERING	- 90% completed
PAINTING	- (only 1 st coat putty completed)
ELECTRICAL WORK	- 30% completed
FIRE FIGHTING WORK	- 10% completed

PROGRESS BHUBANESWAR AS ON 15 JUN 2017



CONNECTING SLAB (B2 & B3 BLOCK)

PROGRESS: Slab shuttering work in progress.

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

EXTERNAL SERVICES



UNDER GROUND RESERVOIR- (Overall completion-30.25%)

PROGRESS: Pump room slab casted.

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

BOUNDARY WALL




BOUNDARY WALL- (Overall completion- 53.5%)

PROGRESS: Copping casting & clamp fixing work in progress

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

SWIMMING POOL

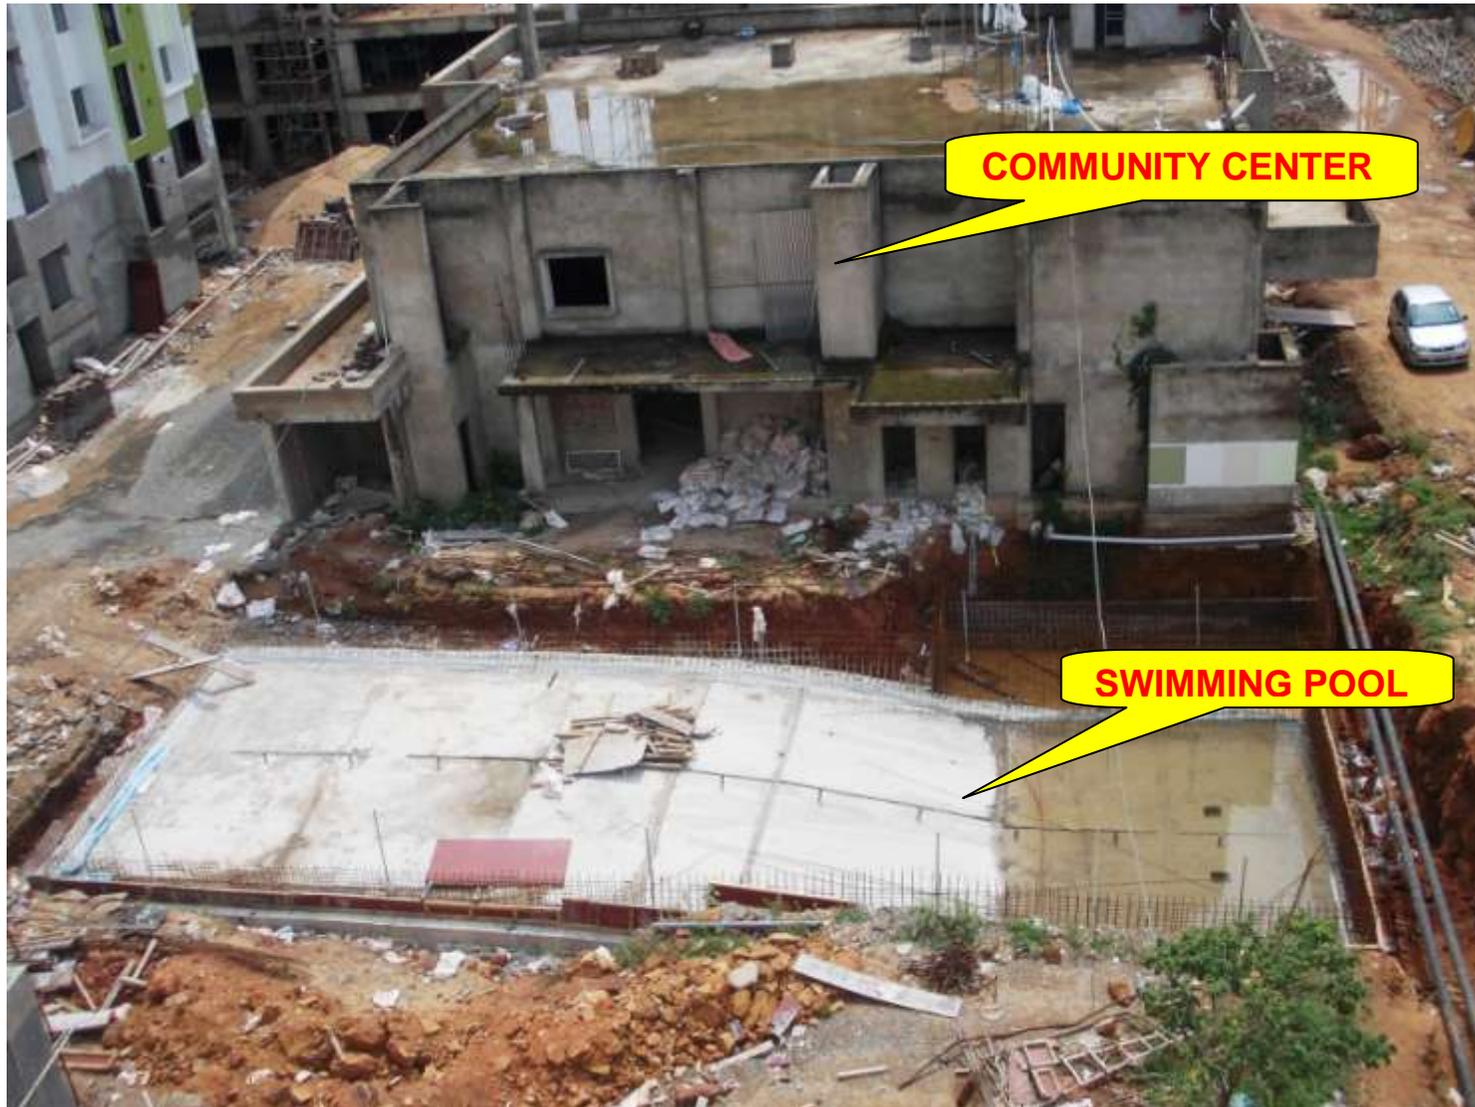

SWIMMING POOL- (Overall completion- 18%)

PROGRESS: Raft casted & wall reinforcement work in progress.

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

SWERAGE TRETMENT PLANT



SWERAGE TRETMENT PLANT (Overall completion- 23%)

PROGRESS: Raft casted & wall reinforcement work in progress.

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

LIFT WORK



LIFT WORK(Overall completion- 26%)

PROGRESS: 04Nos lift material has arrived at site. And 02nos lift work started at A1 block (Channel fixing).

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

EXTERNAL DRAIN WORK



EXTERNAL DRAIN WORK

PROGRESS: PCC work in progress.

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

EXTERNAL ELECTRICAL AT CESU PREMISES (A)



EXTERNAL ELECTRICAL (PART-A) - (Overall completion- 80%)

<u>PROGRESS:</u>	SP ERECTION	- 100% completed
	DP ERECTION	- 100% completed
	FP ERECTION	- 100% completed
	CONDUCTOR STRINGING	- 100% completed
	CIVIL FOUNDATIONS	-100% completed
	EQUIPMENT ERECTION	- Transformer, VCB, Isolator, CT & PT erected
	STRUCTURE ERECTION	- CT, PT, and Isolator & VCB structure erected
	CABLE LAYING	- 85%
	CABLE END TERMINATION	- 85%
	EARTHING	- 100%

PROGRESS BHUBANESWAR AS ON 15 JUN 2017

EXTERNAL ELECTRICAL AT AFNHB SITE PREMISES (B)



EXTERNAL ELECTRICAL (PART-B) - (Overall completion- 55%)

PROGRESS:

CIVIL FOUNDATIONS	- 95% completed
EQUIPMENT ERECTION	- Transformers, DG sets erection
STRUCTURE ERECTION	- FP & TP erection
CABLE LAYING	- To be done
CABLE END TERMINATION	- To be done
EARTHING	- Completed
OH LINE	-Completed
FENCING WALL	- Continuing
DG FUEL ROOM	- Continuing
