

PROGRESS MEERUT PROJECT AS ON 19 DEC

NEW CONTRACTOR HAS COMMENCED WORK WEF 10 DEC 2017.

THE CONTRACT WITH THE NEW CONTRACTOR WAS CONCLUDED IN RECORD TIME OF ONLY 45 DAYS.

PDC : 30 NOV 2018.




POOJAN PRIOR COMMENCEMENT



LABOUR ENGAGEMENT

PROGRESS MEERUT PROJECT AS ON 19 DEC

WORK COMMENCED BY UMAXE PROJECTS PVT LTD

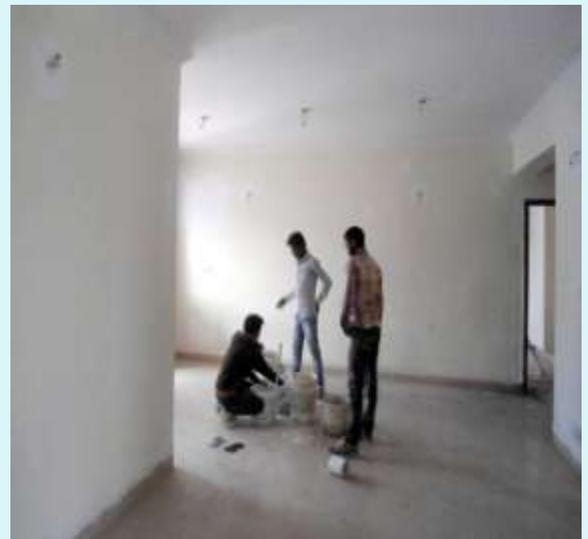

PROGRESS MEERUT PROJECT AS ON 19 DEC



TOWER 1 –

STRUCTURE WORK	100% COMPLETED
BRICK WORK	100% COMPLETED
BALCONY & CORRIDOR RAILING	100% COMPLETED
STAIRCASE RAILING	100% COMPLETED
INTERNAL PLASTER	100% COMPLETED
EXTERNAL PLASTER	100% COMPLETED
PLUMBING WORK	95% COMPLETED
TILING & MARBLE	100% COMPLETED
DOOR WINDOW	80% COMPLETED
INTERNAL PAINTING	70% COMPLETED
EXTERNAL PAINTING	55% COMPLETED
FALSE CEILING	100% COMPLETED
ELECTRICAL WORK	75% COMPLETED
FIRE FIGHTING WORK	65% COMPLETED
CHINAWARE FITTING	90% COMPLETED
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



TOWER 2 –

STRUCTURE WORK	100% COMPLETED
BRICK WORK	100% COMPLETED
BALCONY & CORRIDOR RAILING	100% COMPLETED
STAIRCASE RAILING	100% COMPLETED
INTERNAL PLASTER	100% COMPLETED
EXTERNAL PLASTER	100% COMPLETED
PLUMBING WORK	75% COMPLETED
TILING & MARBLE	85% COMPLETED
DOOR WINDOW	55% COMPLETED
INTERNAL PAINTING	20% COMPLETED
EXTERNAL PAINTING	15% COMPLETED
FALSE CEILING	NIL
ELECTRICAL WORK	50% COMPLETED
FIRE FIGHTING WORK	50% COMPLETED
CHINAWARE FITTING	NIL
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



TOWER 3 –

STRUCTURE WORK	100% COMPLETED
BRICK WORK	90% COMPLETED
BALCONY & CORRIDOR RAILING	95% COMPLETED
STAIRCASE RAILING	95% COMPLETED
INTERNAL PLASTER	95% COMPLETED
EXTERNAL PLASTER	70% COMPLETED
PLUMBING WORK	60% COMPLETED
TILING & MARBLE	20% COMPLETED
DOOR WINDOW	20% COMPLETED
INTERNAL PAINTING	10% COMPLETED
EXTERNAL PAINTING	05% COMPLETED
FALSE CEILING	NIL
ELECTRICAL WORK	40% COMPLETED
FIRE FIGHTING WORK	50% COMPLETED
CHINAWARE FITTING	NIL
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



TOWER 4 –

STRUCTURE WORK	92% COMPLETED
BRICK WORK	90% COMPLETED
BALCONY & CORRIDOR RAILING	90% COMPLETED
STAIRCASE RAILING	95% COMPLETED
INTERNAL PLASTER	75% COMPLETED
EXTERNAL PLASTER	55% COMPLETED
PLUMBING WORK	40% COMPLETED
TILING & MARBLE	10% COMPLETED
DOOR WINDOW	15% COMPLETED
INTERNAL PAINTING	NIL
EXTERNAL PAINTING	05% COMPLETED
FALSE CEILING	NIL
ELECTRICAL WORK	40% COMPLETED
FIRE FIGHTING WORK	50% COMPLETED
CHINAWARE FITTING	NIL
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



TOWER 5 –

STRUCTURE WORK	100% COMPLETED
BRICK WORK	100% COMPLETED
BALCONY & CORRIDOR RAILING	100% COMPLETED
STAIRCASE RAILING	100% COMPLETED
INTERNAL PLASTER	100% COMPLETED
EXTERNAL PLASTER	95% COMPLETED
PLUMBING WORK	70% COMPLETED
TILING & MARBLE	30% COMPLETED
DOOR WINDOW	35% COMPLETED
INTERNAL PAINTING	15% COMPLETED
EXTERNAL PAINTING	10% COMPLETED
FALSE CEILING	NIL
ELECTRICAL WORK	40% COMPLETED
FIRE FIGHTING WORK	50% COMPLETED
CHINAWARE FITTING	NIL
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



TOWER 6 –

STRUCTURE WORK	100% COMPLETED
BRICK WORK	100% COMPLETED
BALCONY & CORRIDOR RAILING	100% COMPLETED
STAIRCASE RAILING	100% COMPLETED
INTERNAL PLASTER	100% COMPLETED
EXTERNAL PLASTER	100% COMPLETED
PLUMBING WORK	90% COMPLETED
TILING & MARBLE	95% COMPLETED
DOOR WINDOW	70% COMPLETED
INTERNAL PAINTING	71% COMPLETED
EXTERNAL PAINTING	45% COMPLETED
FALSE CEILING	80% COMPLETED
ELECTRICAL WORK	75% COMPLETED
FIRE FIGHTING WORK	65% COMPLETED
CHINAWARE FITTING	50% COMPLETED
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



TOWER 7-

STRUCTURE WORK	100% COMPLETED
BRICK WORK	98% COMPLETED
BALCONY & CORRIDOR RAILING	98% COMPLETED
STAIRCASE RAILING	98% COMPLETED
INTERNAL PLASTER	100% COMPLETED
EXTERNAL PLASTER	100% COMPLETED
PLUMBING WORK	80% COMPLETED
TILING & MARBLE	75% COMPLETED
DOOR WINDOW	60% COMPLETED
INTERNAL PAINTING	40% COMPLETED
EXTERNAL PAINTING	18% COMPLETED
FALSE CEILING	NIL
ELECTRICAL WORK	50% COMPLETED
FIRE FIGHTING WORK	60% COMPLETED
CHINAWARE FITTING	NIL
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



TOWER 8-

STRUCTURE WORK	100% COMPLETED
BRICK WORK	100% COMPLETED
BALCONY & CORRIDOR RAILING	100% COMPLETED
STAIRCASE RAILING	100% COMPLETED
INTERNAL PLASTER	100% COMPLETED
EXTERNAL PLASTER	100% COMPLETED
PLUMBING WORK	85% COMPLETED
TILING & MARBLE	80% COMPLETED
DOOR WINDOW	80% COMPLETED
INTERNAL PAINTING	70% COMPLETED
EXTERNAL PAINTING	15% COMPLETED
FALSE CEILING	05% COMPLETED NIL
ELECTRICAL WORK	70% COMPLETED
FIRE FIGHTING WORK	60% COMPLETED
CHINAWARE FITTING	60% COMPLETED
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



COMMUNITY CENTRE –

STRUCTURE WORK	100% COMPLETED
BRICK WORK	100% COMPLETED
BALCONY & CORRIDOR RAILING	100% COMPLETED
STAIRCASE RAILING	100% COMPLETED
INTERNAL PLASTER	100% COMPLETED
EXTERNAL PLASTER	100% COMPLETED
PLUMBING WORK	90% COMPLETED
TILING & MARBLE	100% COMPLETED
DOOR WINDOW	95% COMPLETED
INTERNAL PAINTING	35% COMPLETED
EXTERNAL PAINTING	75% COMPLETED
FALSE CEILING	50% COMPLETED
ELECTRICAL WORK	80% COMPLETED
FIRE FIGHTING WORK	65% COMPLETED
CHINAWARE FITTING	80% COMPLETED
CP FITTINGS	NIL

PROGRESS MEERUT PROJECT AS ON 19 DEC



FACILITY BLOCK –

STRUCTURE WORK	100% COMPLETED
BRICK WORK	100% COMPLETED
STAIRCASE RAILING	100% COMPLETED
INTERNAL PLASTER	100% COMPLETED
EXTERNAL PLASTER	100% COMPLETED
PLUMBING WORK	90% COMPLETED
TILING & MARBLE	90% COMPLETED
DOOR WINDOW	95% COMPLETED
INTERNAL PAINTING	75% COMPLETED
EXTERNAL PAINTING	75% COMPLETED
ELECTRICAL WORK	75% COMPLETED
FIRE FIGHTING WORK	NIL
CHINAWARE FITTING	90% COMPLETED
CP FITTINGS	90% COMPLETED

PROGRESS MEERUT PROJECT AS ON 19 DEC



MAIN GATE & BOUNDARY WALL - 70 % WORK IS COMPLETED

CONFIDENTIAL



ROAD WORK - WBM IN PROGRESS NEAR BLOCK 7&8

PROGRESS – 25 % COMPLETED

PROGRESS MEERUT PROJECT AS ON 19 DEC



STP –

STRUCTURE

100 % COMPLETED

WATER PROOFING OF WALL

100% COMPLETED

BRICK WORK & PLASTER OF MUMTY

100% COMPLETED

WATER PROOFING OF TOP SLAB

100% COMPLETED

PROGRESS MEERUT PROJECT AS ON 19 DEC



SWIMMING POOL –

RCC OF RAFT

70% COMPLETED

PROGRESS MEERUT PROJECT AS ON 19 DEC



Power house - (Overall completion 86.00 %)

Progress – Generators, transformers, HT/LT cables and control panels procured, Awaiting Energising & Installation of Feeder Pillars near Tower 1,2,3 6 7 & 8 .
